Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)
Job Location: Indiana, KY
Contractor: Louisville Paving and Construction

Plant: 100
10/2/2026 9:10:30 AM

Tech: J. Horsley - A
PC: J. Jarvis

Structure ID: 2


P1 BX2424-08BAVF BOX BASE 8inW, 8inF, Variable Ht

P2) 24" x 24" - CASTING HEIGHT - 8"	0 lb
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 22"	2448 lb
1) 24" x 24" - Conseal CS-102 1.00"	0 lb
1) Hole - 20	0 lb
1) Hole - 16	0 lb
1) Hole - 18	0 lb
Structure Total:	2448 lb


Structure Notes: .
KYTC STATE PROJECT
1. 24" X 24" CASTING PROVIDED BY OTHERS.
2. KYTC JUNCTION BOX B1 / PER ASTM C913 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12: C.C.E.W.

Rim: 568.33' Rim to Invert: 2.5' Slack: 0" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	565.83'	90°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"
Invert 2	566.04'	180°	20"	12" CMP	13"	Hole 16	16"	16"	0.52"	0"
Invert 3	566.04'	270°	20"	12" HDPE	14.5"	Hole 18	18"	18"	-0.48"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

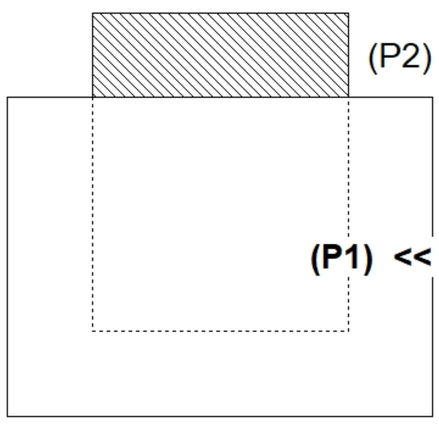


RIGHT-SIDE UP VIEW (int. dimensions)

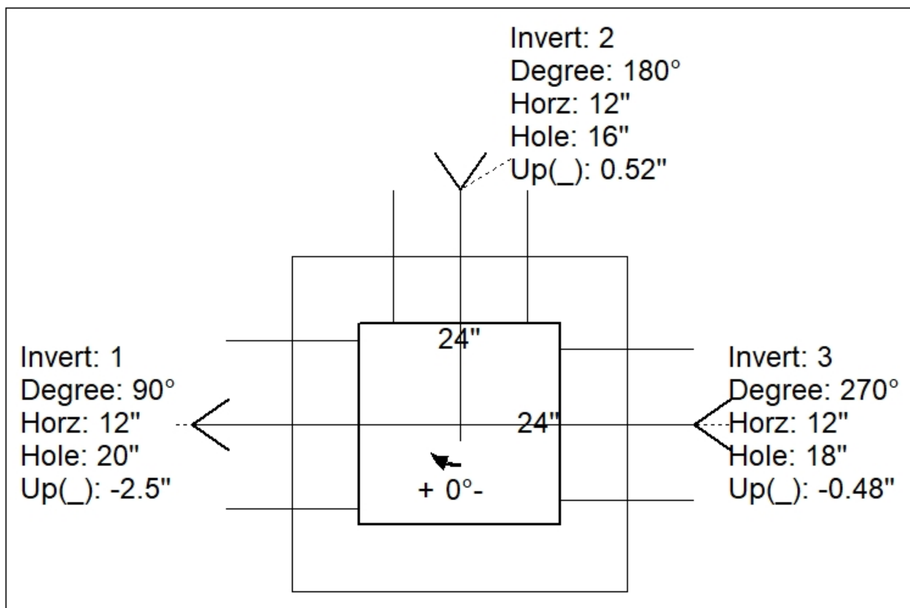

UPSIDE-DOWN VIEW (int. dimenions)

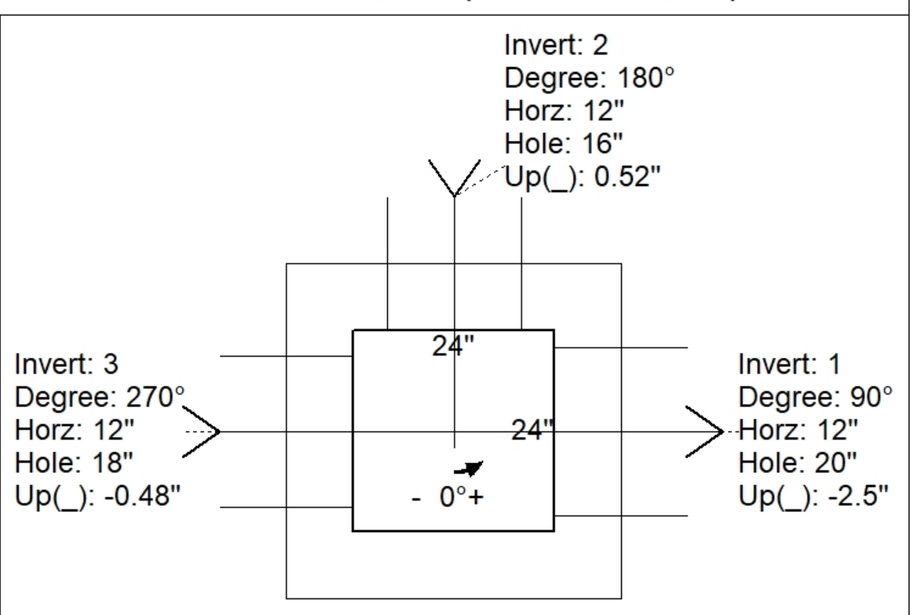

INSIDE WALL DIMENSIONS

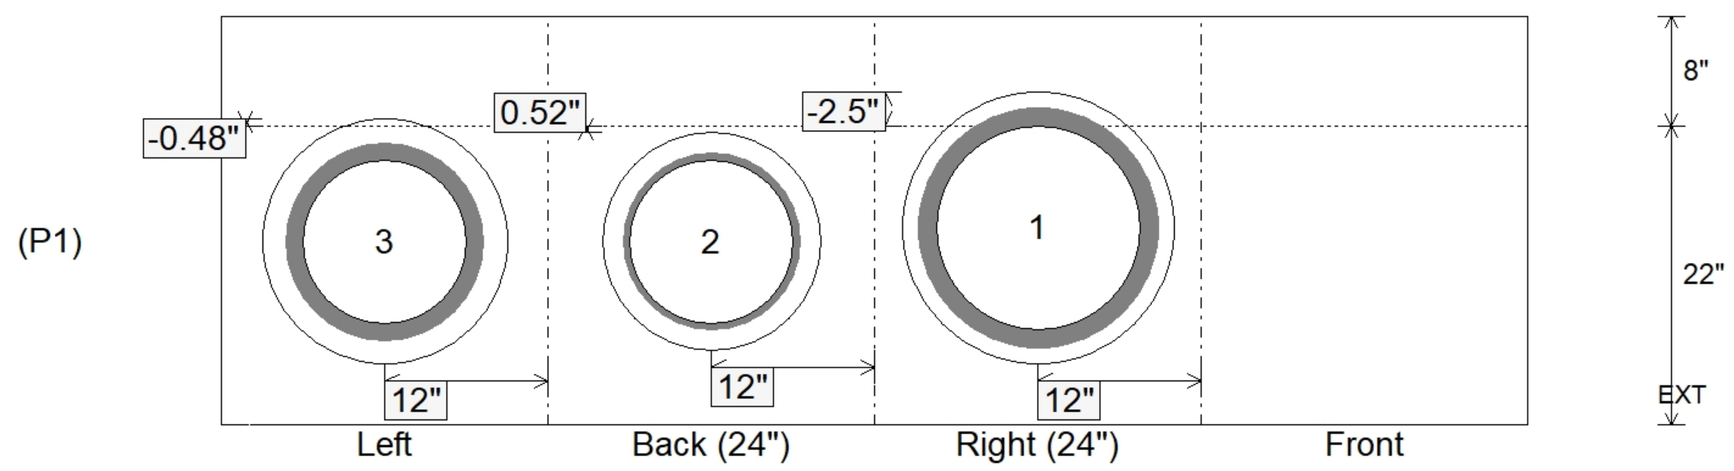

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 22" Height (Ext): 30"	Weight (Net): 2448 lb Volume (Net): 0.62cu.yd
