Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction	Plant: 100 6/17/2026 4:39:38 PM	Tech: J. Horsley - A PC: J. Jarvis	

Structure ID: 57

P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht T/n

P3) 24" x 30" - P.I.P. - BY OTHERS - 8"	0 lb
P2) 24" x 30" - BOX RISER 8inW F/G - 30"	2668 lb
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 31"	3693 lb
2) 24" x 30" - Conseal CS-102 1.00"	0 lb
2) Hole - 24	0 lb
1) Hole - 16	0 lb
2) Hole - 4	0 lb
Structure Total:	6361 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC DBI TYPE 16G / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS

Rim: 551.84' Rim to Invert: 5.75' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	546.09'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-3"	0"
Invert 2	546.09'	180°	20"	18" HDPE	21.2"	Hole 24	24"	24"	-3"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

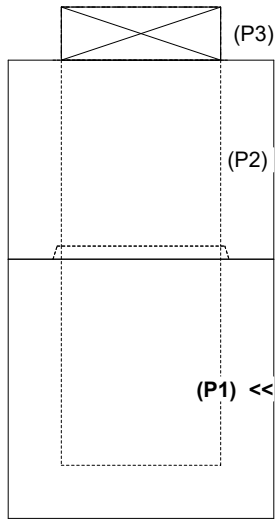

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

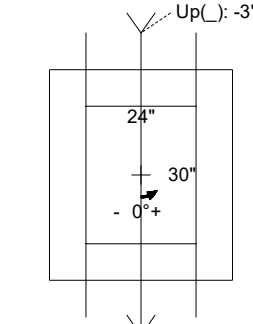

INSIDE WALL DIMENSIONS

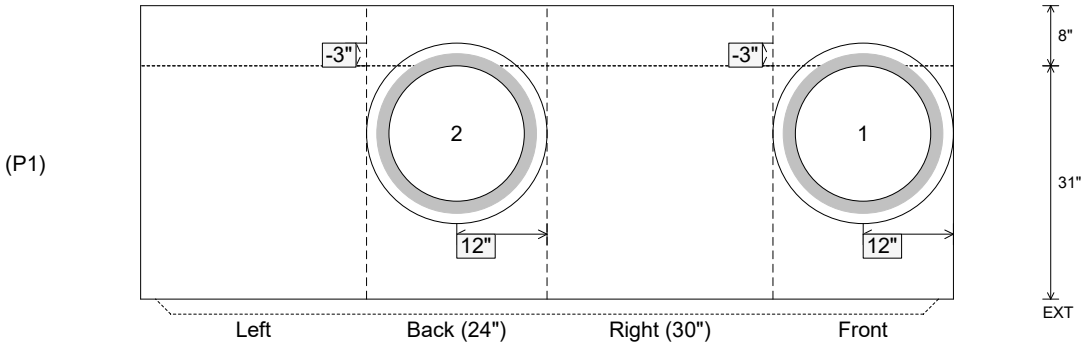

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 31" Height (Ext): 39"	Weight (Net): 3693 lb Volume (Net): 0.94cu.yd
