Job Name: 25-3304 - Vuteq Warehouse Expansion Job Location: Georgetown, KY Contractor: Brown General Contractors	Plant: 100 3/19/2026 11:42:09 AM	Tech: Jared - A PC: Erica Bradley	

Structure ID: ST-10

P2 MH048RS48 MH RISER T/G

P5) 24" - CASTING HEIGHT - 7"	0 lb
P4) 48" - ECC CONE w/ 24" HOLE F/G - 24"	1550 lb
P3) 48" - MH RISER T/G - 48"	3156 lb
P2) 48" - MH RISER T/G - 48"	3353 lb
P1) 48" - MH BASE T/n - 42"	3668 lb
1) CASTING - HOE MCB-315-B Fr./Bar Grate	255 lb
3) 48" - Conseal CS-102 1.00"	0 lb
1) Hole - 32	0 lb
1) Hole - 24	0 lb
1) Hole - 26	0 lb
13) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	11982 lb

Structure Notes:
1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: PER ASTM A615
4. STEPS AT 180 DEGREES
5. HOE MCB-315-B FRAME & BAR GRATE SUPPLIED BY ICAST

Rim: 921.92' Rim to Invert: 14.02' Slack: 2.24" Sump: 3" Step Position: 180°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

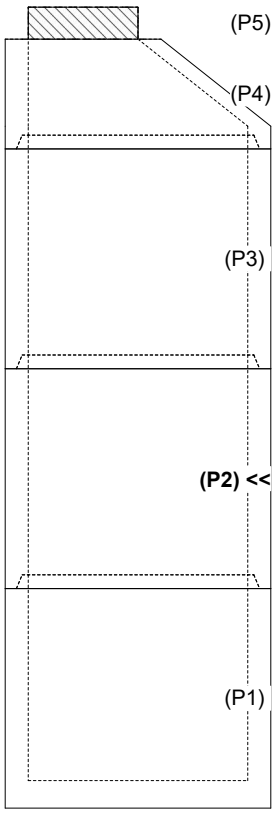

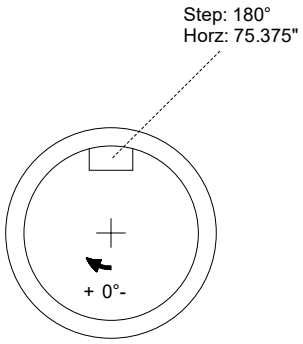

INSIDE WALL DIMENSIONS

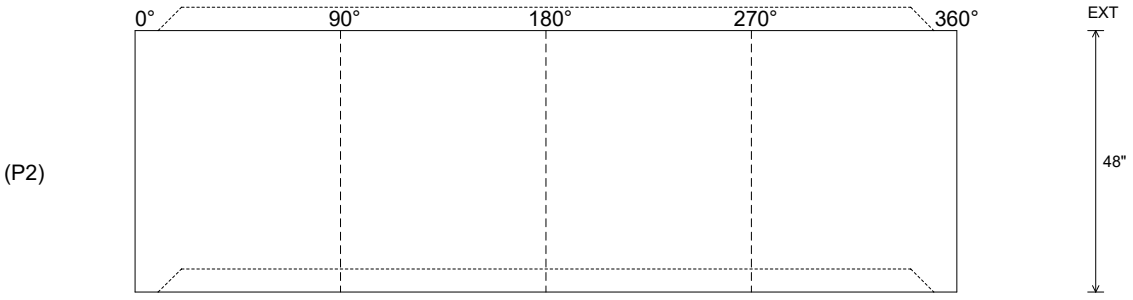

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
