Job Name: 25-3310 - Mammoth Cave NP-MACA 12 Job Location: Mammoth Cave , KY Contractor: Phillips Brothers	Plant: 100 4/2/2026 7:50:01 PM	Tech: J. Horsley - F PC: C. Goff	

Structure ID: IN2

P1 BX3636-08BA36 BOX BASE 8inW, 8inF F/n

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"	0 lb
P1) 36" x 36" - BOX BASE 8inW, 8inF F/n - 36"	5708 lb
1) 36" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 26	0 lb
2) Hole - 2	0 lb
Structure Total:	5708 lb

Structure Notes:
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS (KY-316).
5. #5 DOWELS @ 12" O.C. STUBBED 12" OUT THE TOP OF THE WALLS FOR APRON & GUTTER ATTACHMENT BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 6" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 6" C.C.E.W.

Rim: 738.95' Rim to Invert: 3.66' Slack: -0.08" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	735.29'	0°	26"	18" RCP B WALL	23"	Hole 26	26"	26"	-2.5"	0"
Invert 2	737.28'	90°	26"	2" WEEP HOLE	2"	Hole 2	2"	2"	23.875"	0"
Invert 3	737.28'	270°	26"	2" WEEP HOLE	2"	Hole 2	2"	2"	23.875"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

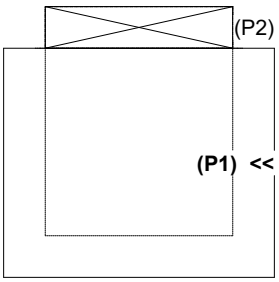

RIGHT-SIDE UP VIEW (int. dimensions)

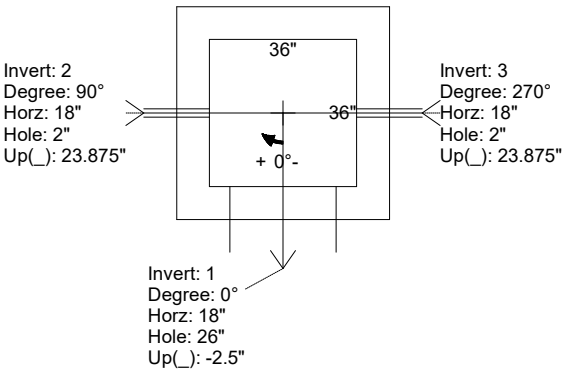

UPSIDE-DOWN VIEW (int. dimenions)

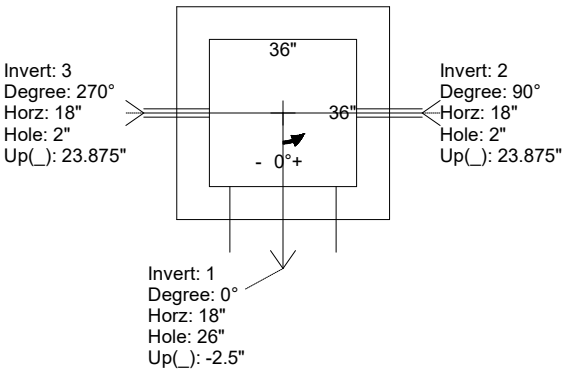

INSIDE WALL DIMENSIONS

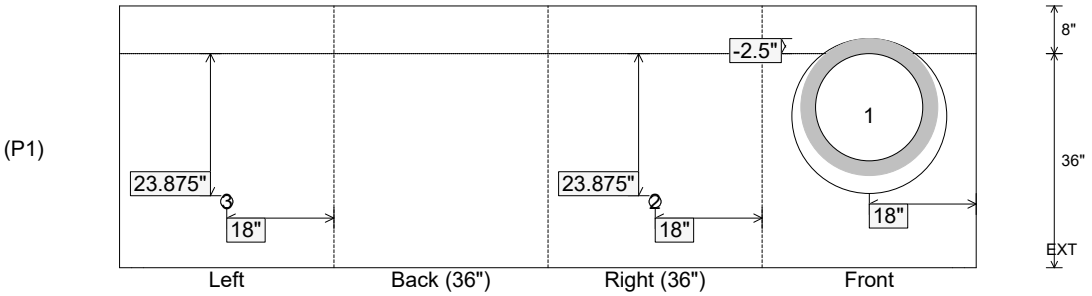

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 5708 lb Volume (Net): 1.46cu.yd
