Job Name: 25-4299 - Seneca High School
Job Location: Louisville, KY
Contractor: Dan Cristiani Excavating Co. Inc.

PC: J. Jarvis
TECH: J. Horsley
Plant: 100

Structure ID: **A10 Top Slab Remake**

Spec: MSD	Rim: 485.5'	Sump: 0"	Floor (Bot): 484.5'
Type: CI DOUBLE	Invert: 485.5'	Floor (Top): 484.5'	Overall Height: 1'
Size: 36" x 60"	Rim to Invert: 0'	Floor Height: 0"	Slack: 0"

Structure Notes: 1. PER LOUISVILLE MSD / ASTM C-913 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT:
- FLAT LID #5 BAR @ 6" C.C. E.W. (GRADE 60)
- BASE: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. NO STORM INVERT
5. NO STEPS
6. HOE 470 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS

STRUCTURE SUMMARY:

P2) 24" x 36" - CASTING HEIGHT - 6"	0 lb
P1) 36" x 60" - CB FLAT TOP 8"W w/24"x36" HOLE - 6"	1555 lb
1) SECONDARY POUR	0 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
Structure Total:	1555 lb

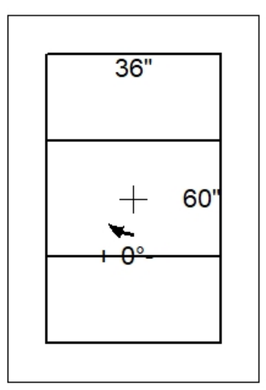

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (_)	Ref
Rim	485.5'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions





Submittal Drawing
7/2/2026 9:01:25 AM

SUBMITTAL
APPROVED BY:
