Job Name: 25-4503 TM Retail Job Location: Somerset, KY Contractor: Weddle Enterprises, Inc	Plant: 100 12/16/2025 2:13:13 PM	Tech: J. Horsley PC: C. Goff	

Structure ID: DI 7 (8)

P2 MH048LD07-18x36RECT MH FLAT TOP w/18"x36" Hole F/F

P3) 18" x 36" - CASTING HEIGHT - 5.5"	0 lb
P2) 48" - MH FLAT TOP w/18"x36" Hole F/F - 7"	1171 lb
P1) 48" - MH BASE Custom Ht F/n - 29"	3086 lb
1) 48" - SGL 1"x14.5' Butyl (2x)	0 lb
2) Hole - 20	0 lb
Structure Total:	4257 lb

Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE 580 F/G).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB = H20 LOADING.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

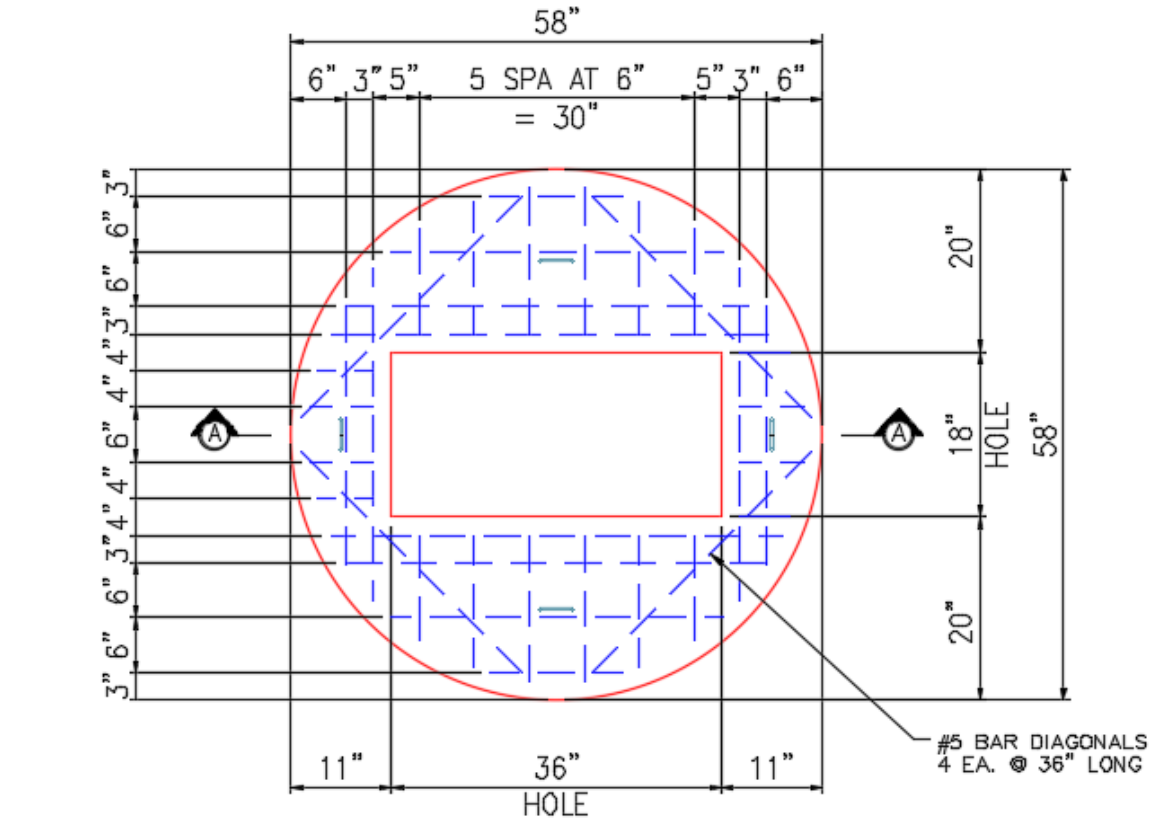

PLAN VIEW

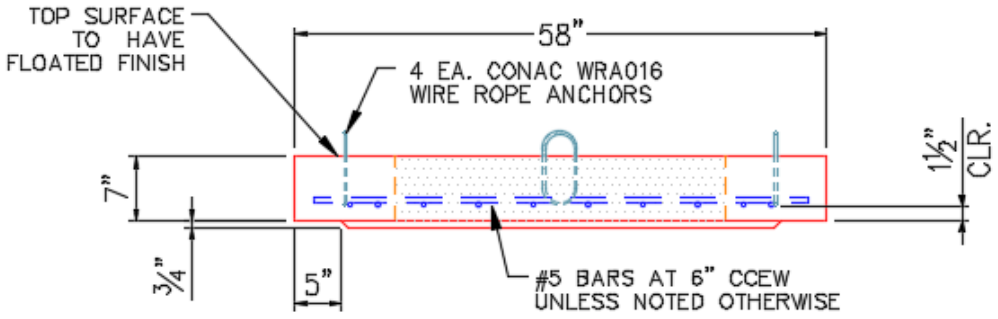

SECTION A-A

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 5"	Height (Ext): 7"	Weight (Net): 1171 lb Volume (Net): 0.3cu.yd
