Job Name: 26-1038 - Perryville & Junction City WW Improvements Job Location: Danville, KY Contractor: Connhurst, LLC	Plant: 100 5/6/2026 4:06:52 PM	Tech: Jared - A PC: E. Bradley	

Structure ID: 61038 (4)

P2 MH096RS54 MH RISER T/G

P6) 42" x 55" - HATCH (CAST FLUSH) - 3"	0 lb
P5) 96" - MH FLAT TOP w/42"x55" Hatch F/G - 17"	8820 lb
P4) 96" - MH RISER Custom Ht T/G - 67"	16574 lb
P3) 96" - MH RISER T/G - 72"	17851 lb
P2) 96" - MH RISER T/G - 54"	13452 lb
P1) 96" - MH SEPARATE BASE-T EXT. 14" (142" OD) T/n - 12"	19580 lb
1) This Structure Includes a Cast-in Item - 42" x 55" Hatch (Supplied by Others)	0 lb
4) JOINT WRAP - 12" WD x 096" MAC WRAP	0 lb
4) 96" - Conseal CS-231 1.00" (Double)	0 lb
3) PSX - 8QRS-S NYLO	20 lb
1) PSX - 12-08 NYLO	8 lb
Structure Total:	76305 lb

Structure Notes:
1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,500 PSI AT 28 DAYS
3. REINFORCEMENT: PER ASTM A615
4. NO STEPS
5. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AT 0°, 90°, 180°, & 270°, 16" FROM TOP OF WALLS

Rim: 963.5' Rim to Invert: 10.85' Slack: 0" Sump: 74.8" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

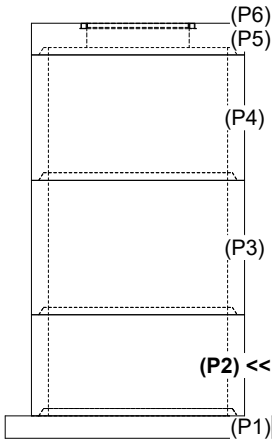



INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 9" Floor Height: 0"	Height (Int): 54" Height (Ext): 54"	Weight (Net): 13452 lb Volume (Net): 3.44cu.yd
