Job Name: 26-1222 Woodvale Subdivision Ph.120-211-300
Job Location: Erlanger, KY
Contractor: Mago Construction Co. LLC

Plant: 100
3/2/2026 1:34:35 PM

Tech: Jared - A
PC: Celina Goff

Structure ID: CB-87-10 CB3A

P1 MH048BAVF MH BASE Custom Ht T/n

P3) 24" x 24" - CASTING HEIGHT - 3.50"	0 lb
P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12"	1500 lb
P1) 48" - MH BASE Custom Ht T/n - 47"	4183 lb
1) CASTING - HOE 410 F/G	228 lb
1) 48" - Conseal CS-102 1.00"	0 lb
1) 24" x 24" - Conseal CS-102 1.00"	0 lb
1) Hole - 24	0 lb
1) Hole - 20	0 lb
1) Hole - 16	0 lb
1) Hole - 6	0 lb
4) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	5911 lb

Structure Notes:
PLAN LABEL: 87
1. HOE 410 F/G PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 896.68' Rim to Invert: 5.24' Slack: 1.98" Sump: 1.6" Step Position: 75°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	891.44'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"
Invert 2	891.69'	150°	75.922"	15" HDPE	17.6"	Hole 20	20"	20.629"	3.3"	0"
Invert 3	891.94'	240°	121.475"	12" HDPE	14.5"	Hole 16	16"	16.312"	6.35"	0"
Invert 4	893.68'	240°	121.475"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6.016"	28.08"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

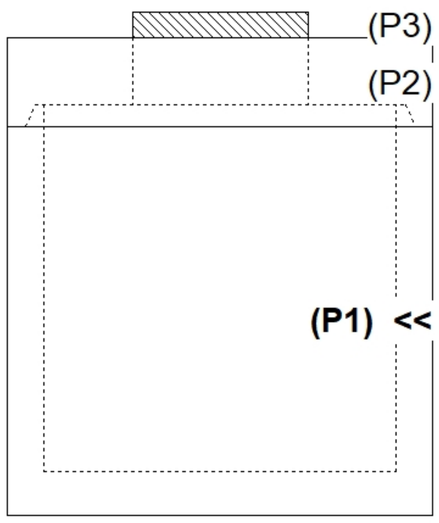

RIGHT-SIDE UP VIEW (int. dimensions)

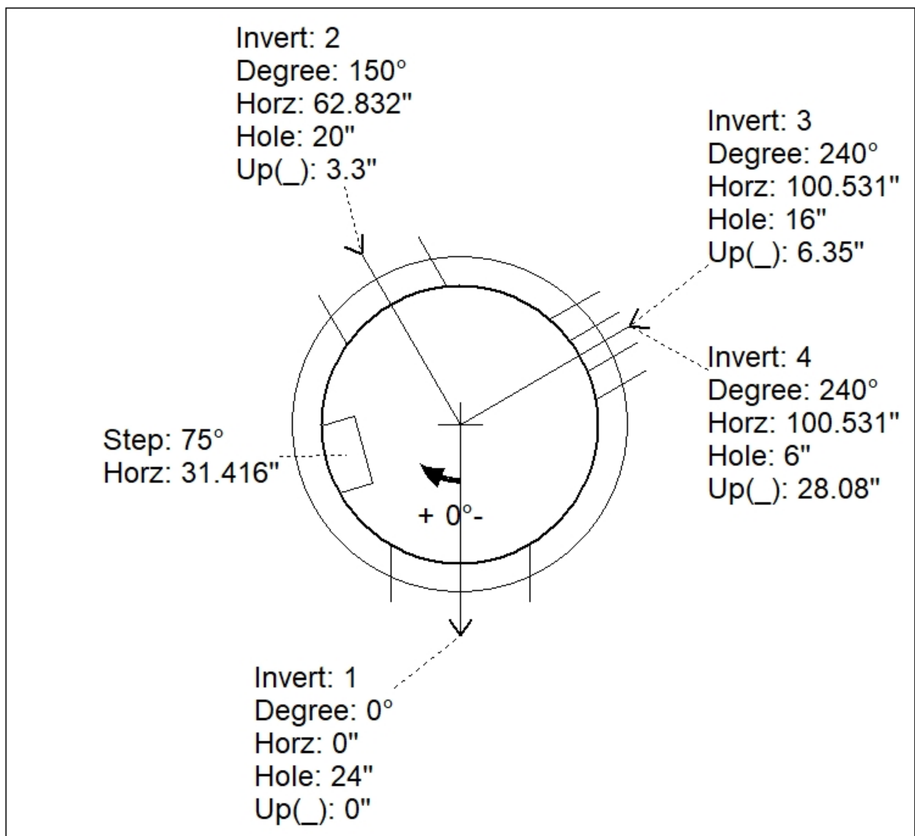

UPSIDE-DOWN VIEW (int. dimenions)

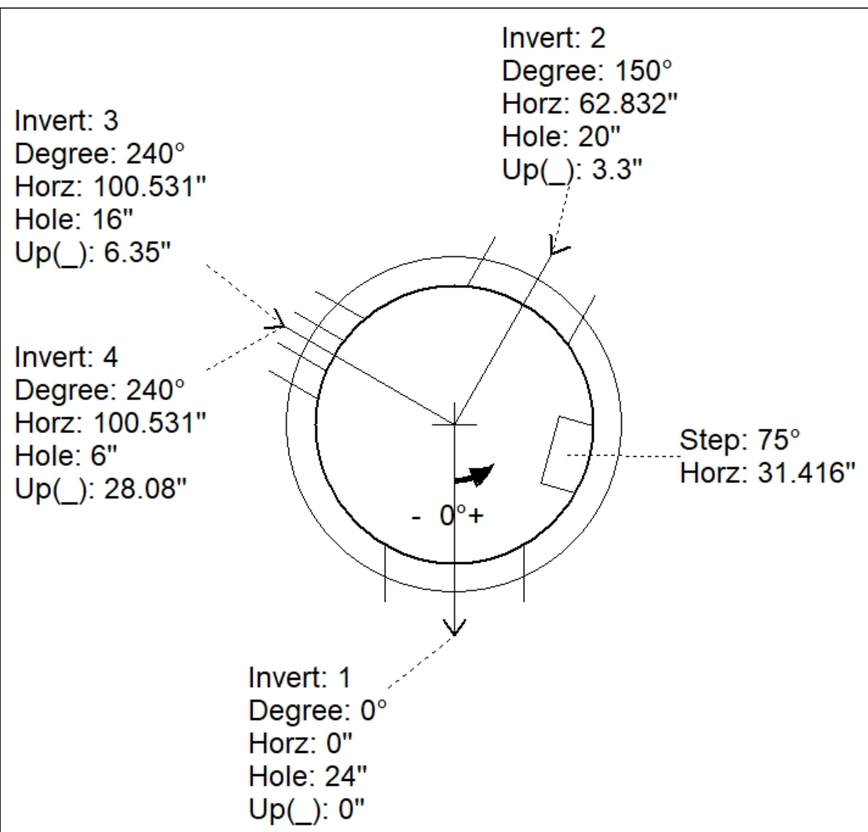

INSIDE WALL DIMENSIONS

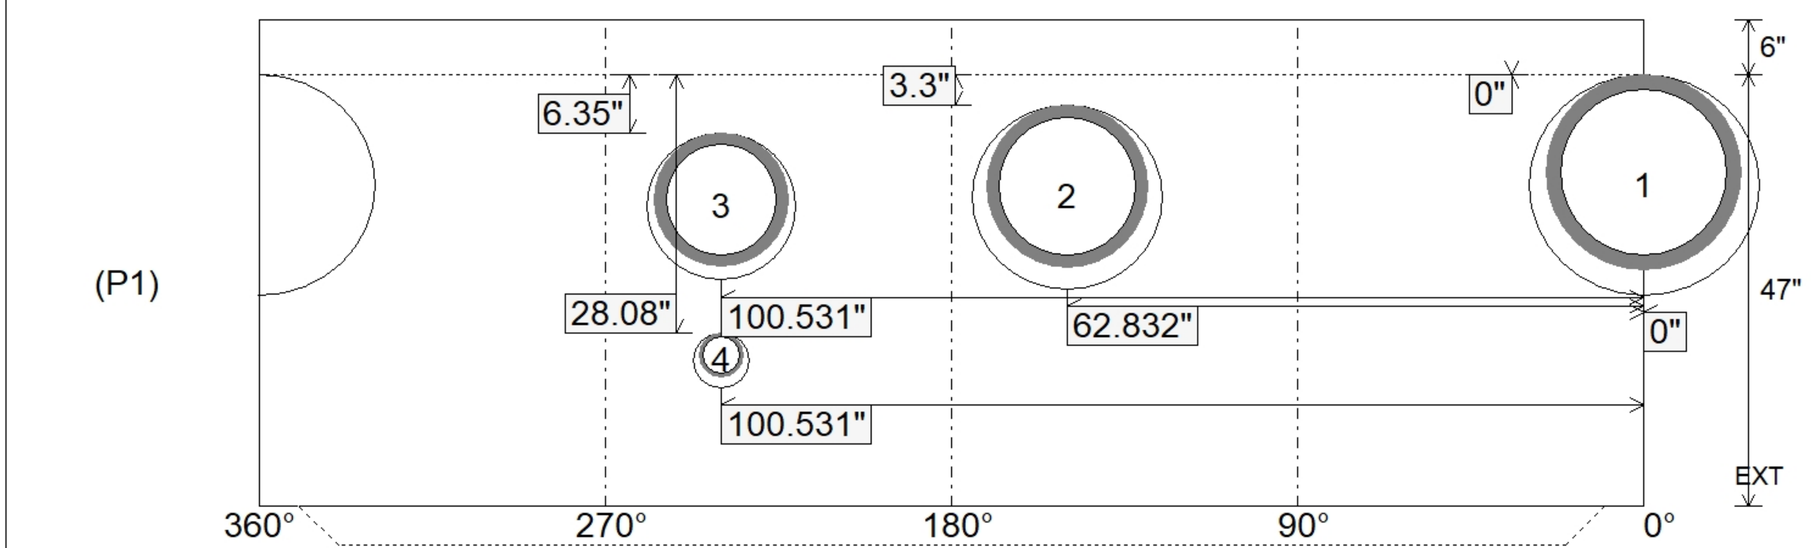

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 47" Height (Ext): 53"	Weight (Net): 4183 lb Volume (Net): 1.07cu.yd
