Job Name: 26-1230 - Wheelwright WWTP & LS Improvements
Job Location: Wheelwright, KY
Contractor: Endesol, Inc.

PC: E. Bradley
TECH: Jared - F
Plant: 100

Structure ID: **WW Top**

Spec: Sanitary	Rim: 1.25'	Sump: 0"	Floor (Bot): 0'
Type: SAN.MH	Invert: 1.25'	Floor (Top): 0'	Overall Height: 1.25'
Size: 72"	Rim to Invert: 0'	Floor Height: 0"	Slack: 0"

Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. HATCH SUPPLIED BY ICAST (HALLIDAY W1S 30"x48").

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .31) #5 BARS AT 6" C.C.E.W.

STRUCTURE SUMMARY:

P2) 30" x 48" - HATCH (CAST FLUSH) - 0"	100 lb
P1) 72" - MH FLAT TOP w/30"x48" Hatch - 15"	4186 lb
1) JOINT WRAP - 12" WD x 072" MAC WRAP	0 lb
1) HATCH (Alum.) - HALLIDAY W1S 30"x48"	85 lb
1) 30" x 48" - Conseal CS-231 1.00" (Double)	0 lb
Structure Total:	4371 lb

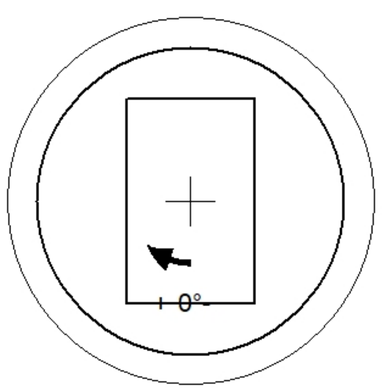

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (_)	Ref
Rim	1.25'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions





Submittal Drawing
5/11/2026 11:08:19 AM

SUBMITTAL
APPROVED BY:
