Job Name: 26-1394 - TMMI Ryder Lift Station Job Location: Princeton, IN Contractor: Koberstein Contracting, Inc.	Plant: 100 7/16/2026 2:29:00 PM	Tech: Jared - A PC: A. Chambers	

Structure ID: 5 MV (2)

P3 MH060LD13S MH FLAT TOP w/37"x36" Hatch F/G

P4) 37" x 36" - HATCH (CAST FLUSH) - 3"	0 lb
P3) 60" - MH FLAT TOP w/37"x36" Hatch F/G - 13"	2305 lb
P2) 60" - MH RISER T/G - 54"	5637 lb
P1) 60" - MH BASE w/FLANGE (08F/08EF) T/n - 41"	8287 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) This Structure Includes a Cast-in Item - 37" x 36" Hatch (Supplied by Others)	0 lb
1) SECONDARY POUR - Extended Base Flange	0 lb
2) 60" - Conseal CS-102 1.00" (Double)	0 lb
3) PSX - 8QRS-S NYLO	20 lb
Structure Total:	16249 lb

Structure Notes:

1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. USF FABRICATION 37" X 36" (36" X 36" CLEAR OPENING) HATCH SUPPLIED BY OTHERS - TO BE CAST INTO FLAT LID
5. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN
6. TOP SURFACE TO RECEIVE LIGHT BRUSH FINISH

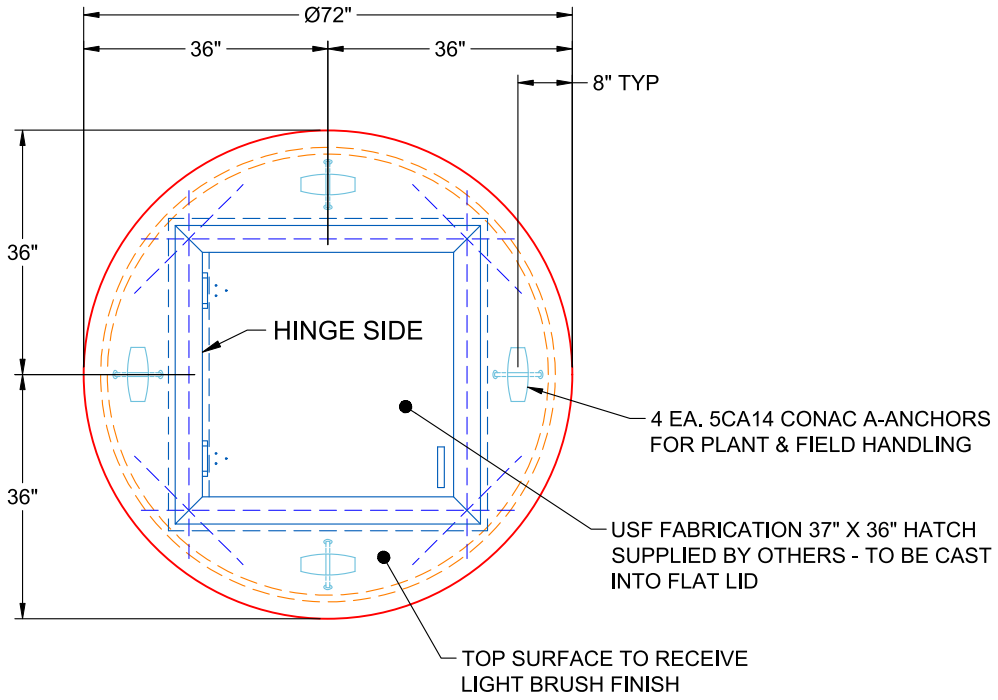

PLAN VIEW
(RIGHT SIDE UP)



FRONT VIEW
(RIGHT SIDE UP)



SIDE VIEW
(RIGHT SIDE UP)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 6"	Height (Ext): 13"	Weight (Net): 2305 lb Volume (Net): 0.59cu.yd

Job Number:

26-1394

Job Name:

TMMI Ryder Lift Station

Structure:

5 MV (2)

Note:

USF Fabrication 37” x 36” Hatch Supplied By Others To Be Cast Into Flat Lid
