Job Name: 26-1635 - KYTC Oldham Co (261505) - P2
Job Location: Peewee Valley, KY
Contractor: Cleary Construction, Inc.

PC: T. Ryan
TECH: Jared - F
Plant: 100

Structure ID: **17055-40 CBIA-19**

Spec: KYTC	Rim: 838.66'	Sump: 0"	Floor (Bot): 832.253'
Type: CBI TYPE A (10')	Invert: 832.92'	Floor (Top): 832.92'	Overall Height: 6.083'
Size: 24" x 36"	Rim to Invert: 5.74'	Floor Height: 8"	Slack: 3.88"

Structure Notes: .
** KYTC STATE PROJECT **
1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)).
.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"	3398 lb
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"	5270 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 37"	4982 lb
1) CASTING - HOE KY-206 F/C (KY CBI A)	206 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb
1) Hole - 6	0 lb
Structure Total:	13856 lb

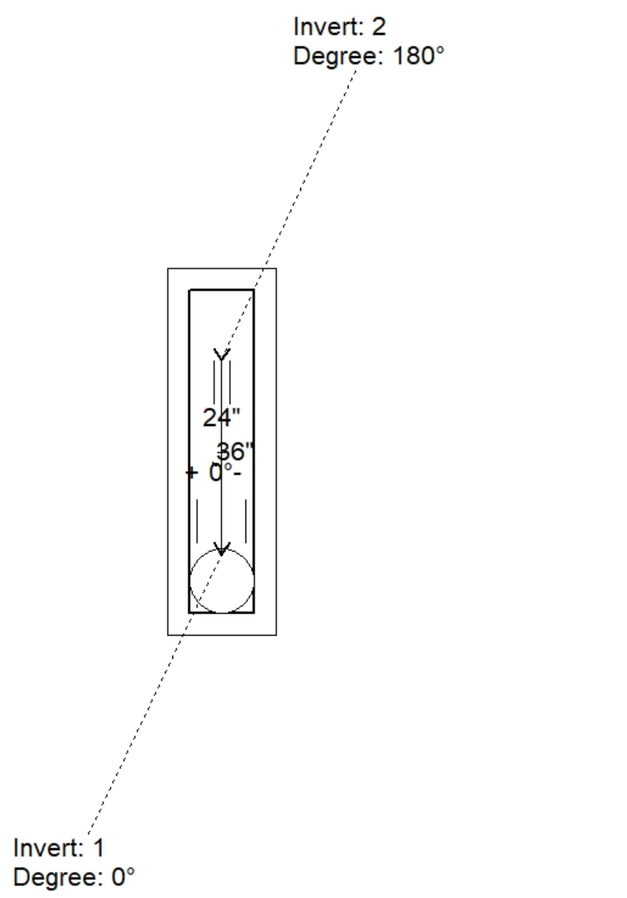

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (_)	Ref
Rim	838.66'							
Reducer								
Invert 1	832.92'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2	835.25'	180°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	26.96"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

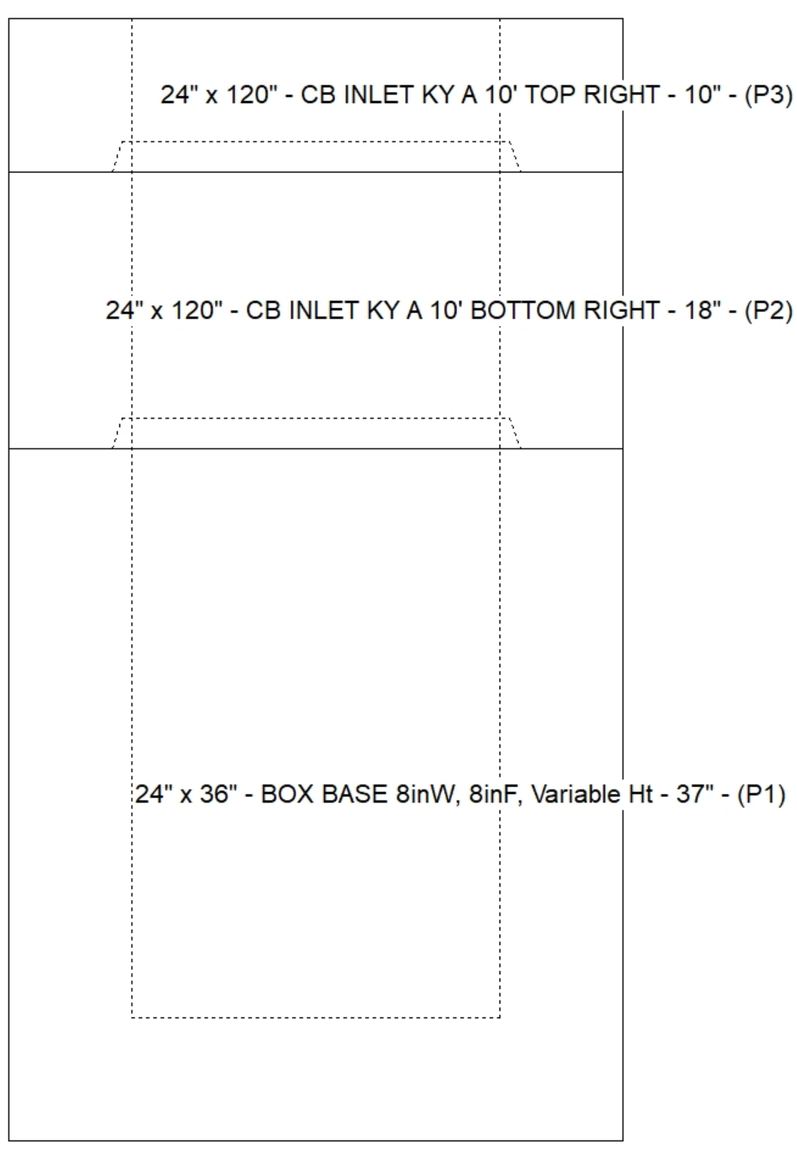

Default - Interior Dimensions

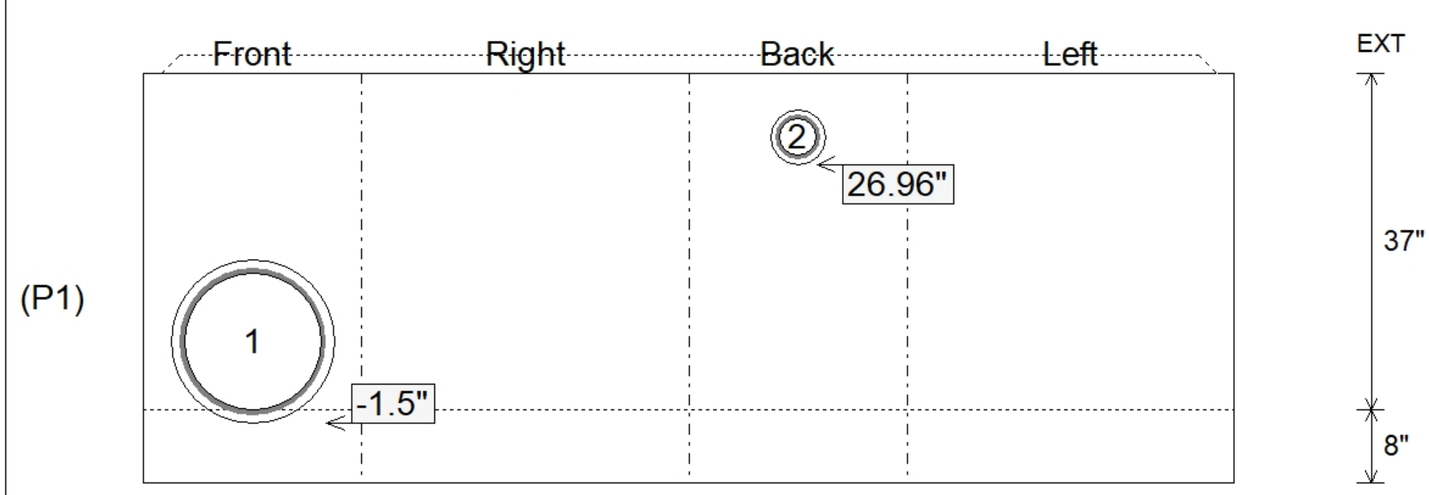

Submittal Drawing
7/28/2026 3:11:02 PM

SUBMITTAL
APPROVED BY:
