Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.	Plant: 100 8/14/2026 1:20:47 PM	Tech: Jared - F PC: T. Ryan	

Structure ID: 51055-141 ST- JB1

P1 BX2424-08BAVF BOX BASE 8inW, 8inF, Variable Ht F/n

P3) CASTING (cast in) - 0	0 lb
P2) 24" x 24" - BX FLAT LID 8inW SPEC. (KY JB-B1) F/F - 8"	770 lb
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 46"	4811 lb
1) 24" x 24" - Conseal CS-102 1.00"	0 lb
1) 24" - Conseal CS-102 1.00"	0 lb
1) Hole - 16	0 lb
1) Hole - 12	0 lb
Structure Total:	5581 lb

Structure Notes: .
***KYTC STATE PROJECT**
1. KYTC JUNCTION BOX B1 / PER ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. TOP SLAB WITH KY-206 CAST-IN (KY-206 SUPPLIED BY OTHERS).
.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12: C.C.E.W.

Rim: 794.8' Rim to Invert: 4.5' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	790.3'	345°	17.75"	12" CMP	13"	Hole 16	16"	16.564"	-2"	3"
Invert 2	790.3'	180°	20"	8" CMP	9"	Hole 12	12"	12"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

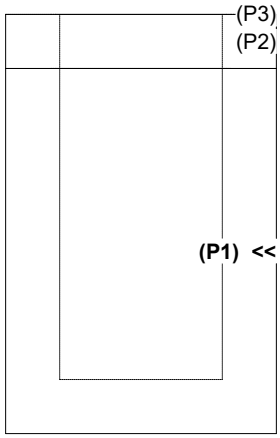

RIGHT-SIDE UP VIEW (int. dimensions)

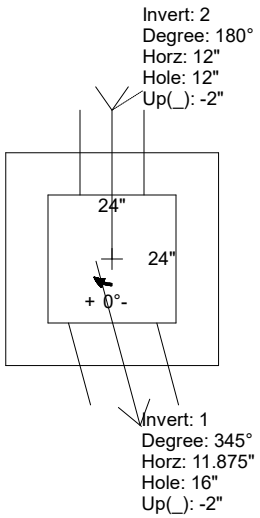

UPSIDE-DOWN VIEW (int. dimenions)

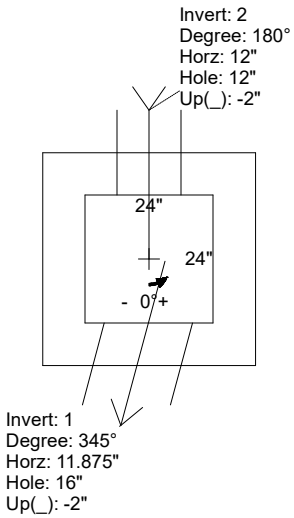

INSIDE WALL DIMENSIONS

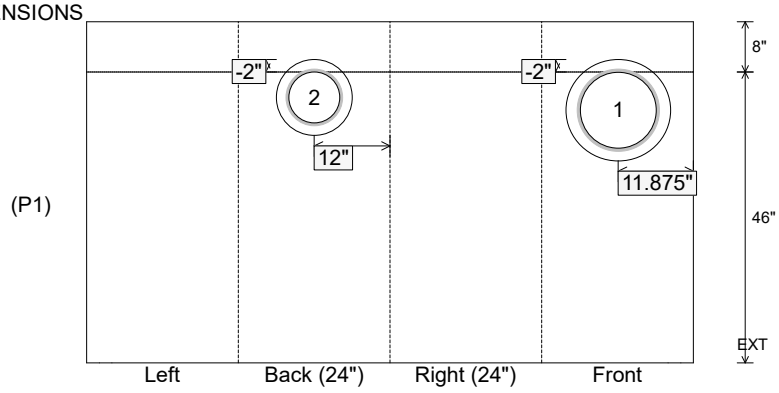

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 46" Height (Ext): 54"	Weight (Net): 4811 lb Volume (Net): 1.23cu.yd
