Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.	Plant: Beaver Dam 9/3/2026 3:15:45 PM	Tech: J. Coppage PC: M. Sullivan	

Structure ID: 1410

P2 MH108RS60 MH RISER

P6) 24" - CASTING HEIGHT - 0"	0 lb
P5) 24" - GRADE RING - 3"	202 lb
P4) 108" - MH FLAT TOP w/24" ECC Hole - 17"	10472 lb
P3) 108" - MH RISER - 54"	16703 lb
P2) 108" - MH RISER - 60"	18664 lb
P1) 108" - MH BASE - 96"	31782 lb
3) 108" - Conseal CS-102 1.00"	0 lb
2) 24" - Conseal CS-102 1.00"	0 lb
1) Hole - 90	0 lb
1) Hole - 76	0 lb
1) Hole - 34	0 lb
4) Hole - 6	0 lb
17) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	77824 lb

Rim: 509.17' Rim to Invert: 18.65' Slack: 0.8" Sump: 7" Step Position: 120

Structure Notes: .
1. (CASTING PROVIDED BY OTHERS)
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .36)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

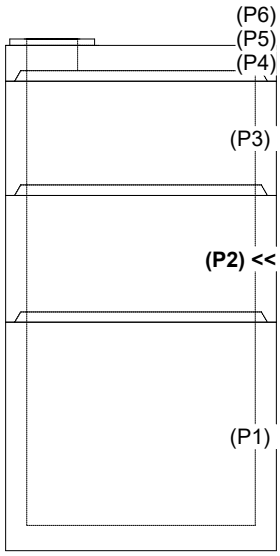

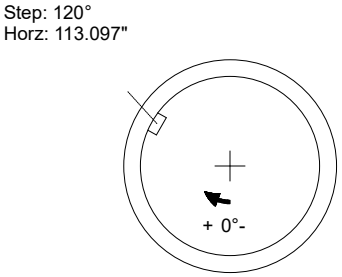

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 10" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 18664 lb Volume (Net): 4.77cu.yd
