Job Name: 26-2104 - Jeffersonville High School Parking Lot Job Location: Jeffersonville, IN Contractor: Mac Construction & Excavating, Inc.	Plant: 100 6/27/2026 7:12:35 PM	Tech: Jared - A PC: T. Lewis	

Structure ID: 3 ST-CI

P1 BX2436-08BA36 BOX BASE 8inW, 8inF F/n

P2) 24" x 36" - CASTING HEIGHT - 6"	0 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF F/n - 36"	4458 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 26	0 lb
1) Hole - 22	0 lb
Structure Total:	4458 lb

Structure Notes:
1. PER ASTM C-913 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. STORM INVERT BY OTHERS
5. HOE 525 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS

Rim: 483.63' Rim to Invert: 3.42' Slack: 1.54" Sump: 2.5" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	480.21'	270°	26"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"
Invert 2	480.51'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	3.875"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

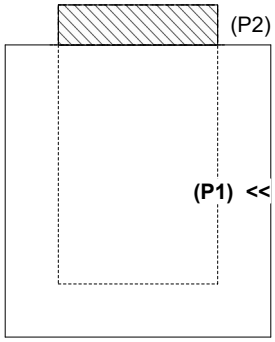

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

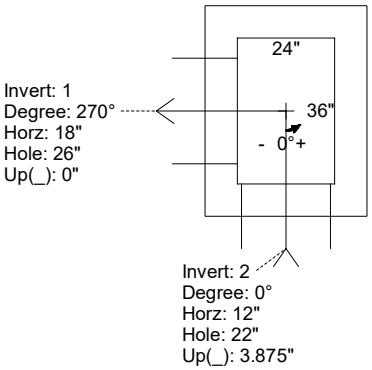

INSIDE WALL DIMENSIONS

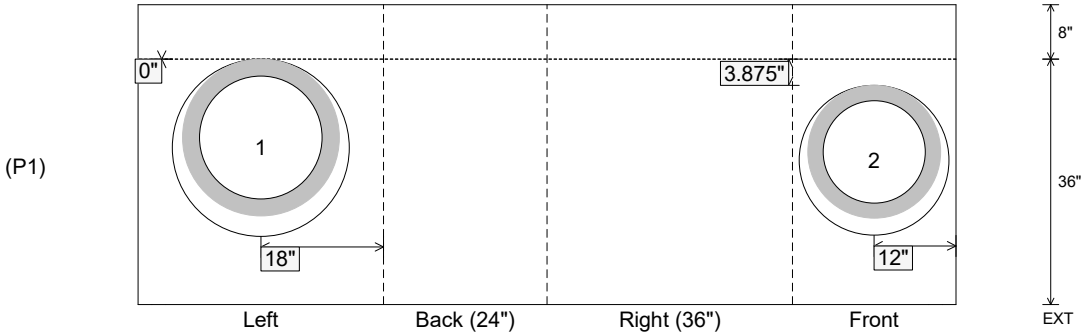

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 4458 lb Volume (Net): 1.14cu.yd
