| | | | |
|---|---|---|---|
| Job Name: 26-2358 - Sidewalk Lighting and Expansion - North Gibson School Corp<br>Job Location: Princeton, IN<br>Contractor: Hahn Excavating, Inc. | Plant: 100<br>7/14/2026 11:23:36 AM | Tech: Jared - F<br>PC: E. Bradley | |

## Structure ID: Str. 2 ST-JB

**P2 BX030030-06LD06-24C CB FLAT TOP 6"W w/24"Hole F/F**

| | |
|---|---|
| P3) 24" - CASTING HEIGHT - 7" | 0 lb |
| P2) 30" x 30" - CB FLAT TOP 6"W w/24"Hole F/F - 6" | 660 lb |
| P1) 30" x 30" - BOX BASE 6inW, 6inF F/n - 30" | 2529 lb |
| 1) CASTING - HOE MC-315 F/C Storm | 258 lb |
| 1) 30" x 30" - Conseal CS-102 1.00" | 0 lb |
| 1) 24" - Conseal CS-102 1.00" | 0 lb |
| 2) Hole - 26 | 0 lb |
| Structure Total: | 3447 lb |

Structure Notes: .
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE MC-315 F/C STORM).

.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

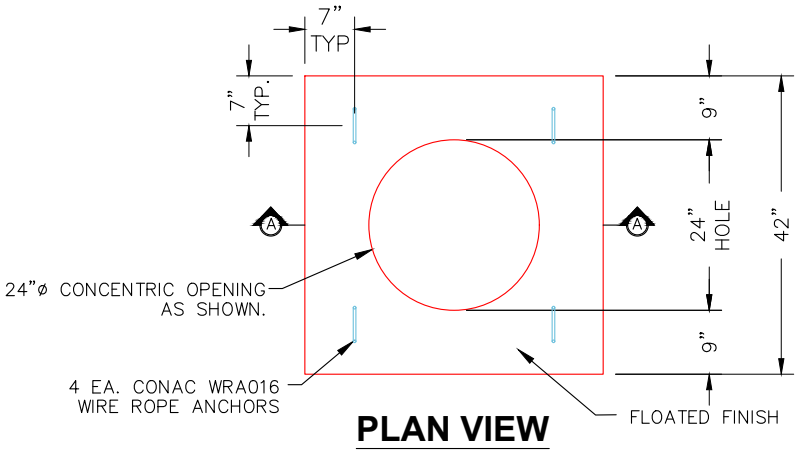


**PLAN VIEW**

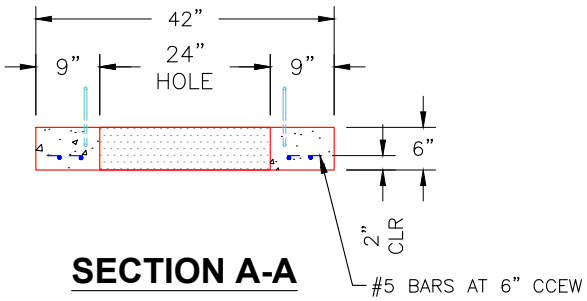


**SECTION A-A**

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

| | | | | |
|---|---|---|---|---|
| Coating (Int):<br>Coating (Ext): | Seam Up: Flat<br>Seam Dn: Flat | Wall Thickness: 6" | Height (Ext): 6" | Weight (Net): 660 lb<br>Volume (Net): 0.17cu.yd |
