Job Name: 26-2495 Campbell View Apartments Vault
Job Location: Bowling Green, KY
Contractor: Core & Main LP (BG)

PC: T. Lewis
TECH: S. Felletter
Plant: Beaver Dam

Structure ID: **QL1**

Spec: Vaults	Rim: 7'	Sump: 20.004"	Floor (Bot): 0'
Type: Meter Vault 6inW, 6inF	Invert: 2.167'	Floor (Top): 0.5'	Overall Height: 7'
Size: 72" x 132"	Rim to Invert: 4.833'	Floor Height: 6"	Slack: 0"

Structure Notes:

STRUCTURE SUMMARY:

P3) 48" x 48" - HATCH (CAST FLUSH) - 3"	100 lb
P2) 72" x 132" - CB FLAT TOP 6"W w/48" X 48" HATCH F/F - 8"	6573 lb
P1) 72" x 132" - BOX BASE 6inW, 6inF, Variable Ht F/n - 70"	21236 lb
1) This Structure Includes a Cast-in Item	0 lb
1) 48" x 48" - Conseal CS-102 1.00" (Double)	0 lb
2) Hole - 6	0 lb
2) Hole - 8	0 lb
Structure Total:	27909 lb

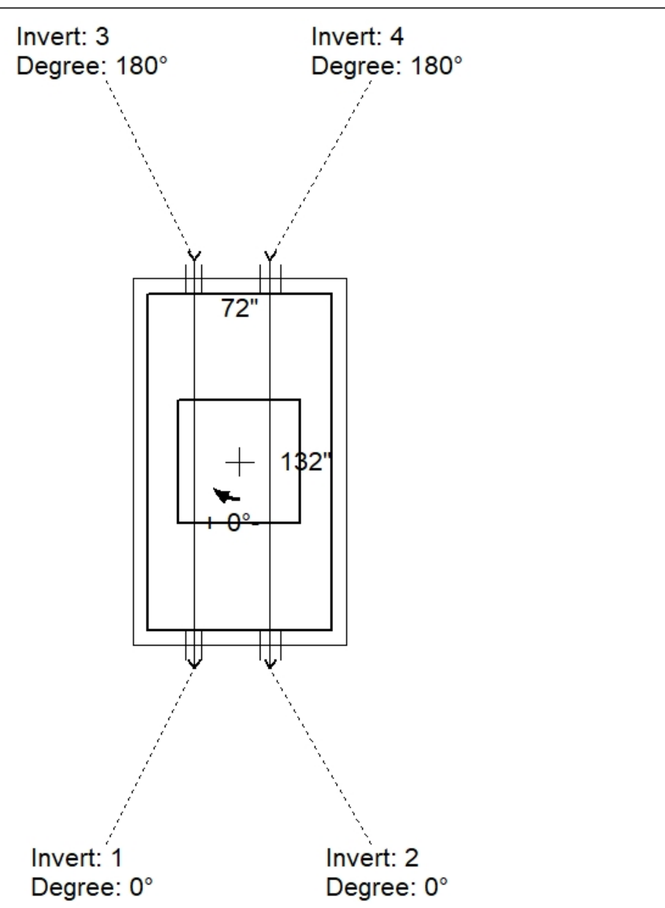

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (_)	Ref
Rim	7'							
Reducer								
Invert 1	2.167'	0°	2" PVC SCH40	2.375"	6"	Hole 6	18.028"	P1
Invert 2	2.167'	0°	4" PVC SCH40	4.5"	8"	Hole 8	18.003"	P1
Invert 3	2.167'	180°	2" PVC SCH40	2.375"	6"	Hole 6	18.028"	P1
Invert 4	2.167'	180°	4" PVC SCH40	4.5"	8"	Hole 8	18.003"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

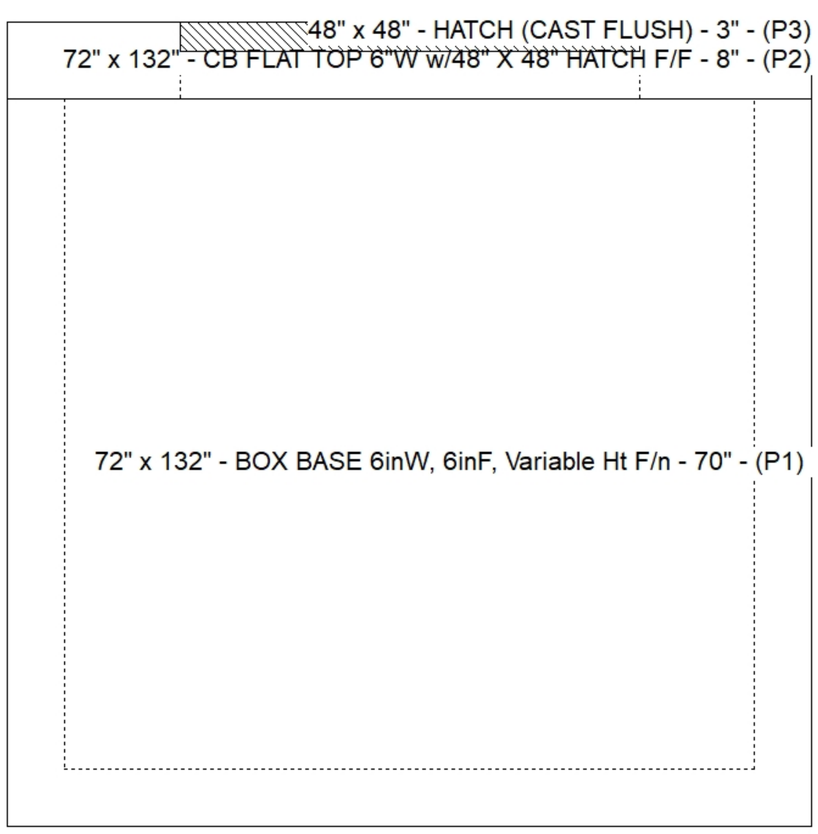

Default - Interior Dimensions

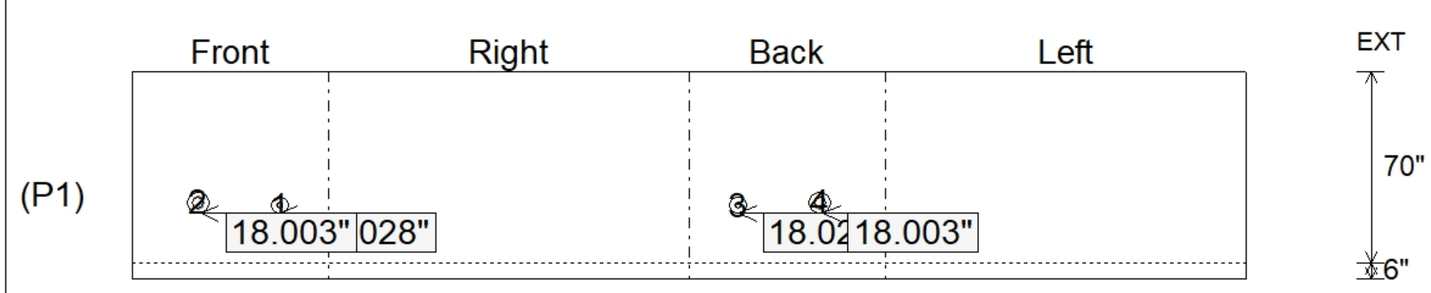

Submittal Drawing
8/13/2026 8:52:31 AM

SUBMITTAL
APPROVED BY:
