Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.	Plant: Beaver Dam 8/24/2026 8:12:06 AM	Tech: J. ROSS PC: E. BRADLEY	

Structure ID: BB2 LEXA

P3 CBITA10LEX-TS — CB INLET LEX A 10' TOP SAG

P3) 36" x 120" - CB INLET LEX A 10' TOP SAG - 12"	2700 lb
P2) 36" x 120" - CB INLET LEX A 10' BOTTOM SAG - 18"	3650 lb
P1) 36" x 36" - BOX BASE 8inW, 8inF - 30"	5066 lb
1) CASTING - HOE KY-206 F/C (KY CBI A)	206 lb
1) 36" x 36" - Conseal CS-102 1.00"	0 lb
1) 24" - Conseal CS-102 1.00"	0 lb
1) Hole - 22	0 lb
2) Hole - 6	0 lb
6) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	11622 lb

Structure Notes: .
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
- TOP PHASE TOP - #5 BARS AT 6" C.C.E.W.
- TOP PHASE BTM - #5 BARS AT 12" C.C.E.W.
- TOP SLAB - #5 BARS AT 12" C.C.E.W..
- RISER/WALLS - #5 BARS AT 12" C.C.E.W.
- FLOOR - #5 BARS AT 12" C.C.E.W.
4. HOE KY-206 F/C CASTING PROVIDED BY ICAST

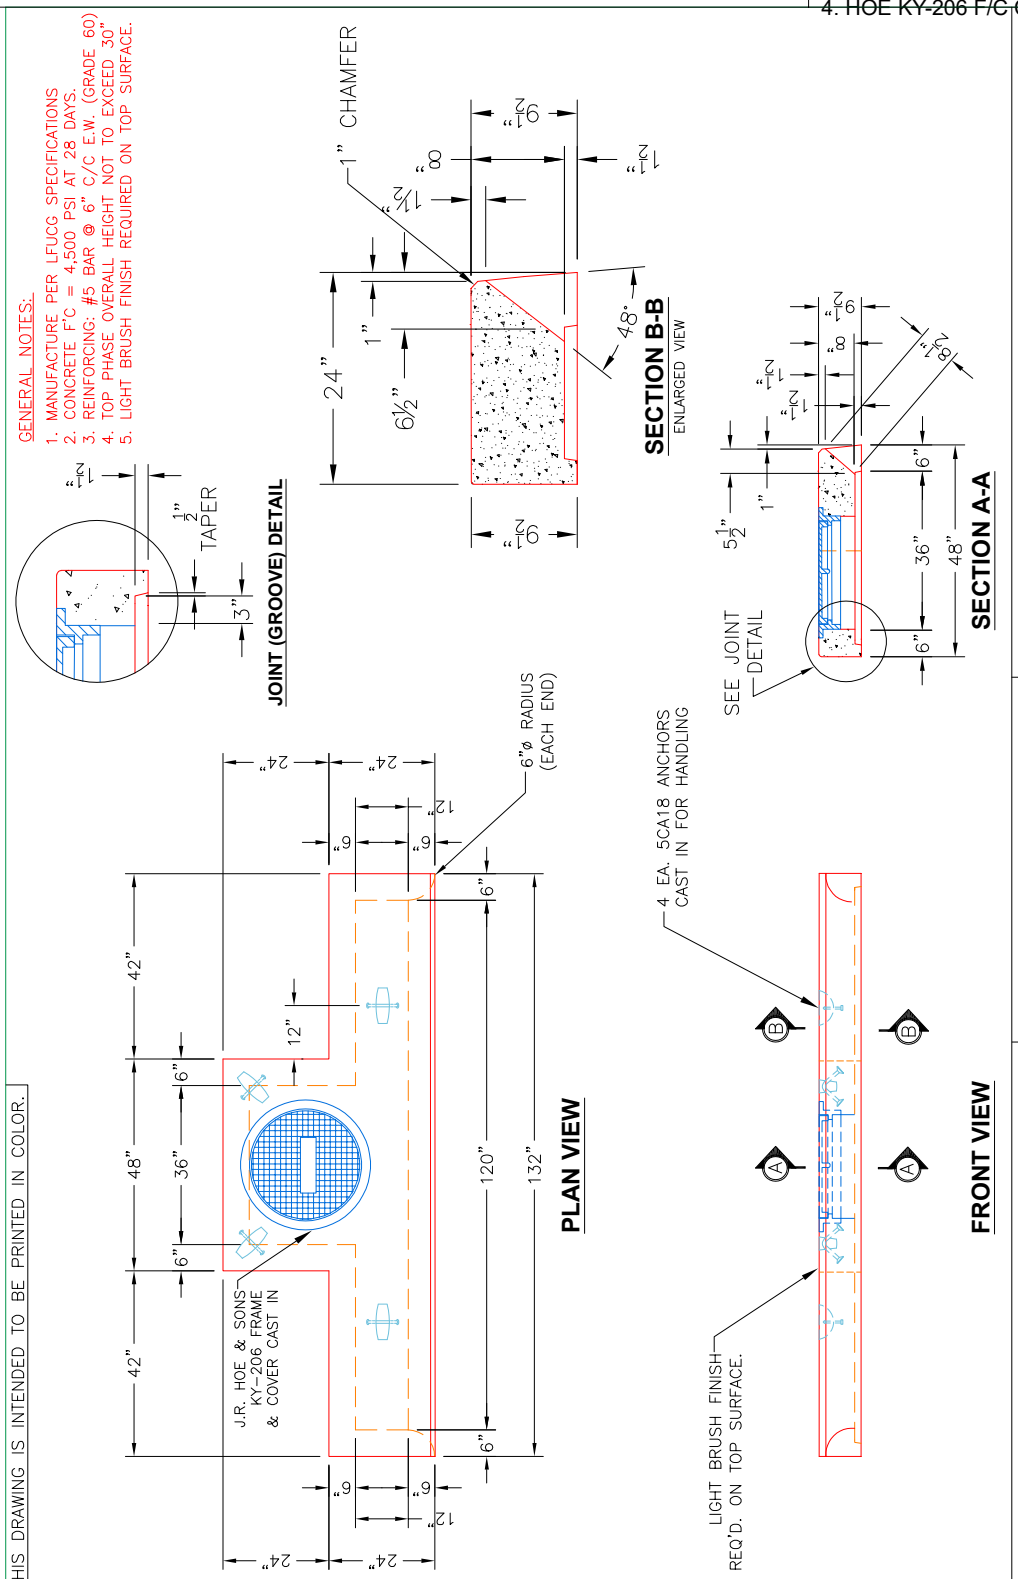

PRODUCT I.D.: CBITA10LEX-TS	DESCRIPTION: LFUCG 10' CBI-TYPE A TOP PHASE TOP (SAG)
PRODUCT VIEW: RIGHT SIDE UP	CUSTOMER: THE ALLEN COMPANY, INC.
PLANT: BEAVER DAM, KY.	PROJECT: ASHTREE SUBDIVISION UNIT 3 PH. 1
WEIGHT: 2,700 LBS.	STRUCTURE ID.: BB2 LEXA
TOP JOINT: N/A	SALES ORDER NO.: 26-2560
BOTTOM JOINT: SHIP-LAP GROOVE	P.C.: J.H. ROSS, PE / DRAWING: N. RICHARDS
QC CHECK INITIALS:	DATE: 8/21/26 / SCALE: NTS / PG. 1 of 1

PRODUCTION WORK ORDER

QUALITY CONTROL CHECKLIST
- ☐ ALL DIMENSIONS CORRECT.
- ☐ LIFTERS INSTALLED.
- ☐ LIGHT BRUSH FINISH ON TOP SURFACE.
- ☐ REINFORCING CORRECT.
- ☐ CASTING CORRECT.
- ☐ LFUCG THROAT CORRECT.
- ☐ ALL PATCHWORK ACCEPTABLE.

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.
