Job Name: 26-3070 - KYTC Barren Co. Call 100 (261130) Job Location: Glasgow, KY Contractor: Cleary Construction, Inc.	Plant: 100 10/8/2026 1:21:12 PM	Tech: Jared - F PC: T. Ryan	

Structure ID: DB3 DBI13G

P2 BX2430-08R36 BOX RISER 8inW F/G

P4) 15" x 27" - P.I.P. - BY OTHERS - 8"	0 lb
P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"	963 lb
P2) 24" x 30" - BOX RISER 8inW F/G - 36"	3366 lb
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 38"	4241 lb
2) 24" x 30" - Conseal CS-102 1.00"	0 lb
1) 15" x 27" - Conseal CS-102 1.00"	0 lb
1) Hole - 28	0 lb
1) Hole - 22	0 lb
2) Hole - 4	0 lb
Structure Total:	8571 lb

Structure Notes: .
KYTC STATE PROJECT
1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. STUB #5 BARS 6" OUT TOP OF SLAB (SPA@12"C/C).
4. CASTING BY OTHERS (HOE KY-230-G F/G (GRADE)).
.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (AS .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT)
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 710.06' Rim to Invert: 7.5' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3	708.06'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	26"	0"
Invert 4	708.06'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	26"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

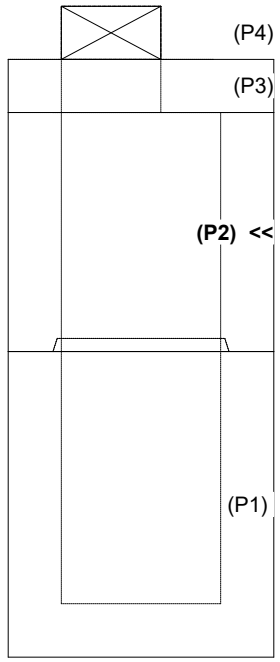

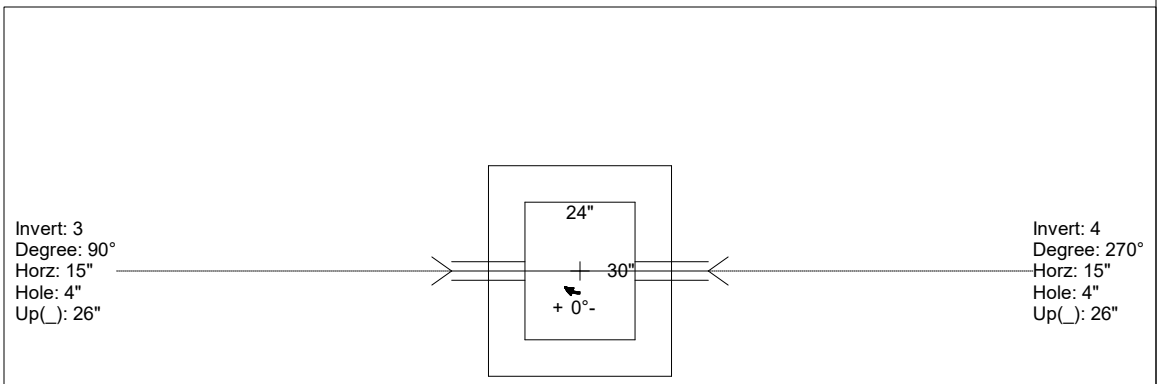

INSIDE WALL DIMENSIONS

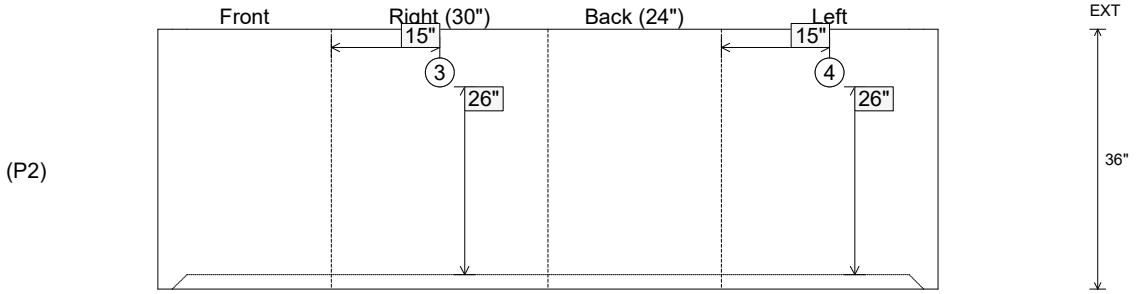

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 3366 lb Volume (Net): 0.86cu.yd
