
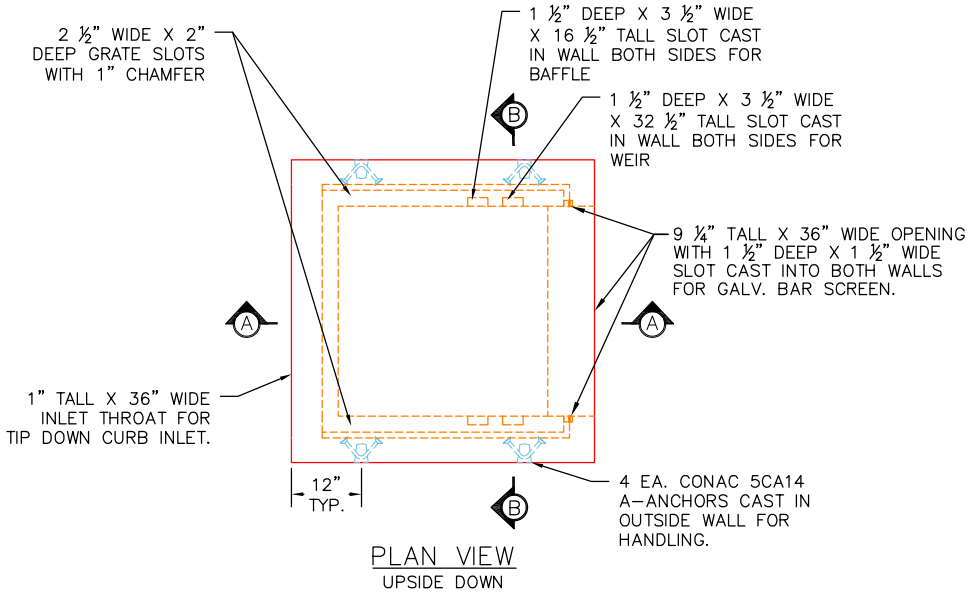



PLAN VIEW
UPSIDE DOWN

GENERAL NOTES:

1. MANUFACTURED TO ASTM C–913 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. REINFORCING: PER ASTM A615. (GRADE 60).
   – WALLS/FLOOR (As. 12) #5 BAR @ 12" C.C.E.W.
   2" MIN. CLEARANCE (TYP)
4. WEIGHTS: TOTAL = 3,924 LBS
5. 41" X 41" X 1.25" GALV. BAR GRATE BY ICAST.
6. 1.25" X 7" X 39" GALV. BAR SCREEN BY ICAST.
7. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE

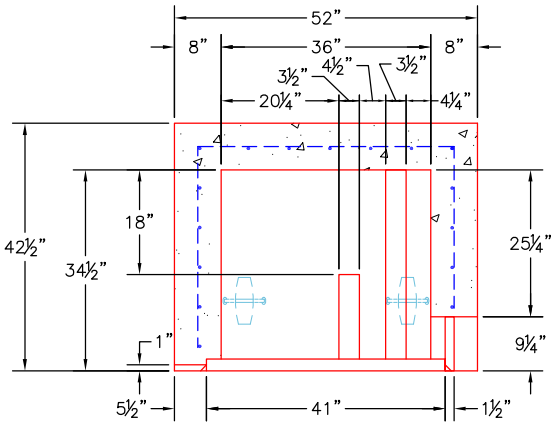

SECTION A–A
UPSIDE DOWN

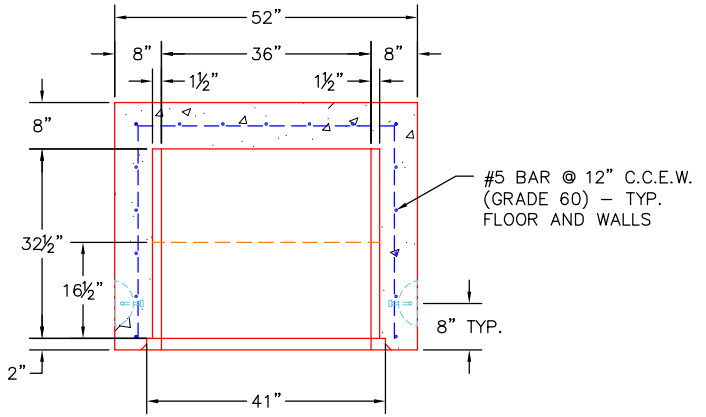

SECTION B–B
UPSIDE DOWN

PRODUCTION WORK ORDER	PRODUCT I.D.: BX036036–08BAVF	DESCRIPTION: 36" X 36" X 34 ½" BOX BASE	
QUALITY CONTROL CHECKLIST	PRODUCT VIEW: UPSIDE DOWN	CUSTOMER: CONVERGENT WATER TECHNOLOGIES	
☐ ALL DIMENSIONS CORRECT. ☐ LIFTERS INSTALLED. ☐ OPENING(S) CORRECT LOCATION. ☐ REINFORCING CORRECT. ☐ SURFACE QUALITY ACCEPTABLE. ☐ EDGES CHAMFERED. ☐ ALL PATCHWORK ACCEPTABLE.	PLANT: BEAVER DAM, KY.	PROJECT: WEST FRANKLIN PARK P02818	
	WEIGHT: 3,924 LBS.	STRUCTURE: C3.1.2	
	TOP SECTION JOINT: FLAT	ORDER NO: 26–3904	
	BASE SECTION JOINT: N/A	PC: C. GOFF	DRAWING: J. HORSLEY
	QC CHECK INITIALS:	DATE: 10/07/26	SCALE: NTS | PG. 1 of 1

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.
